



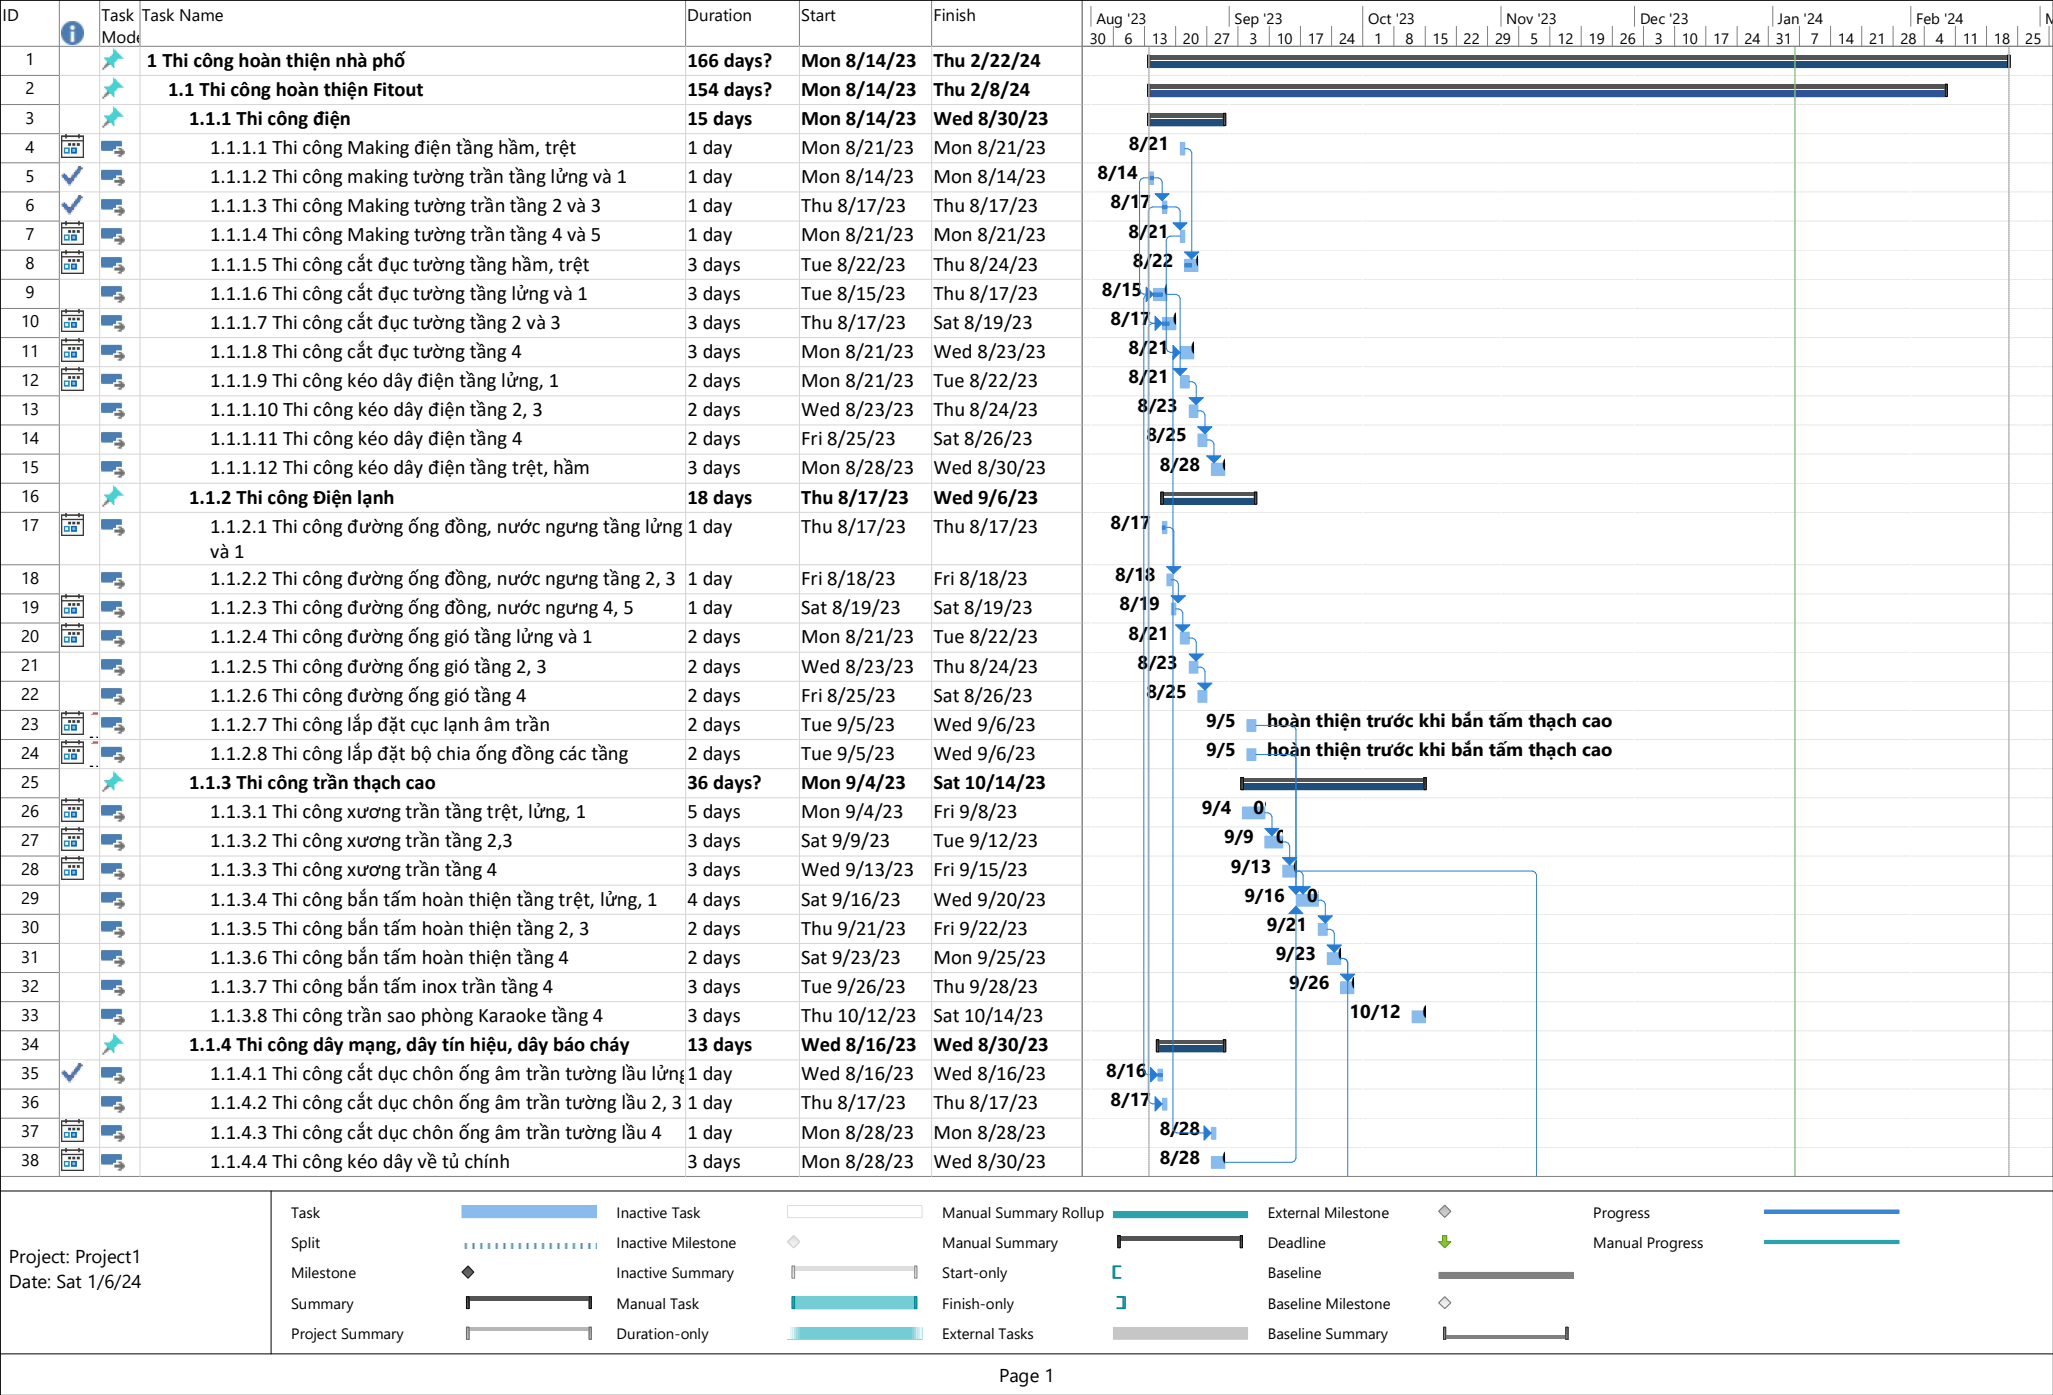

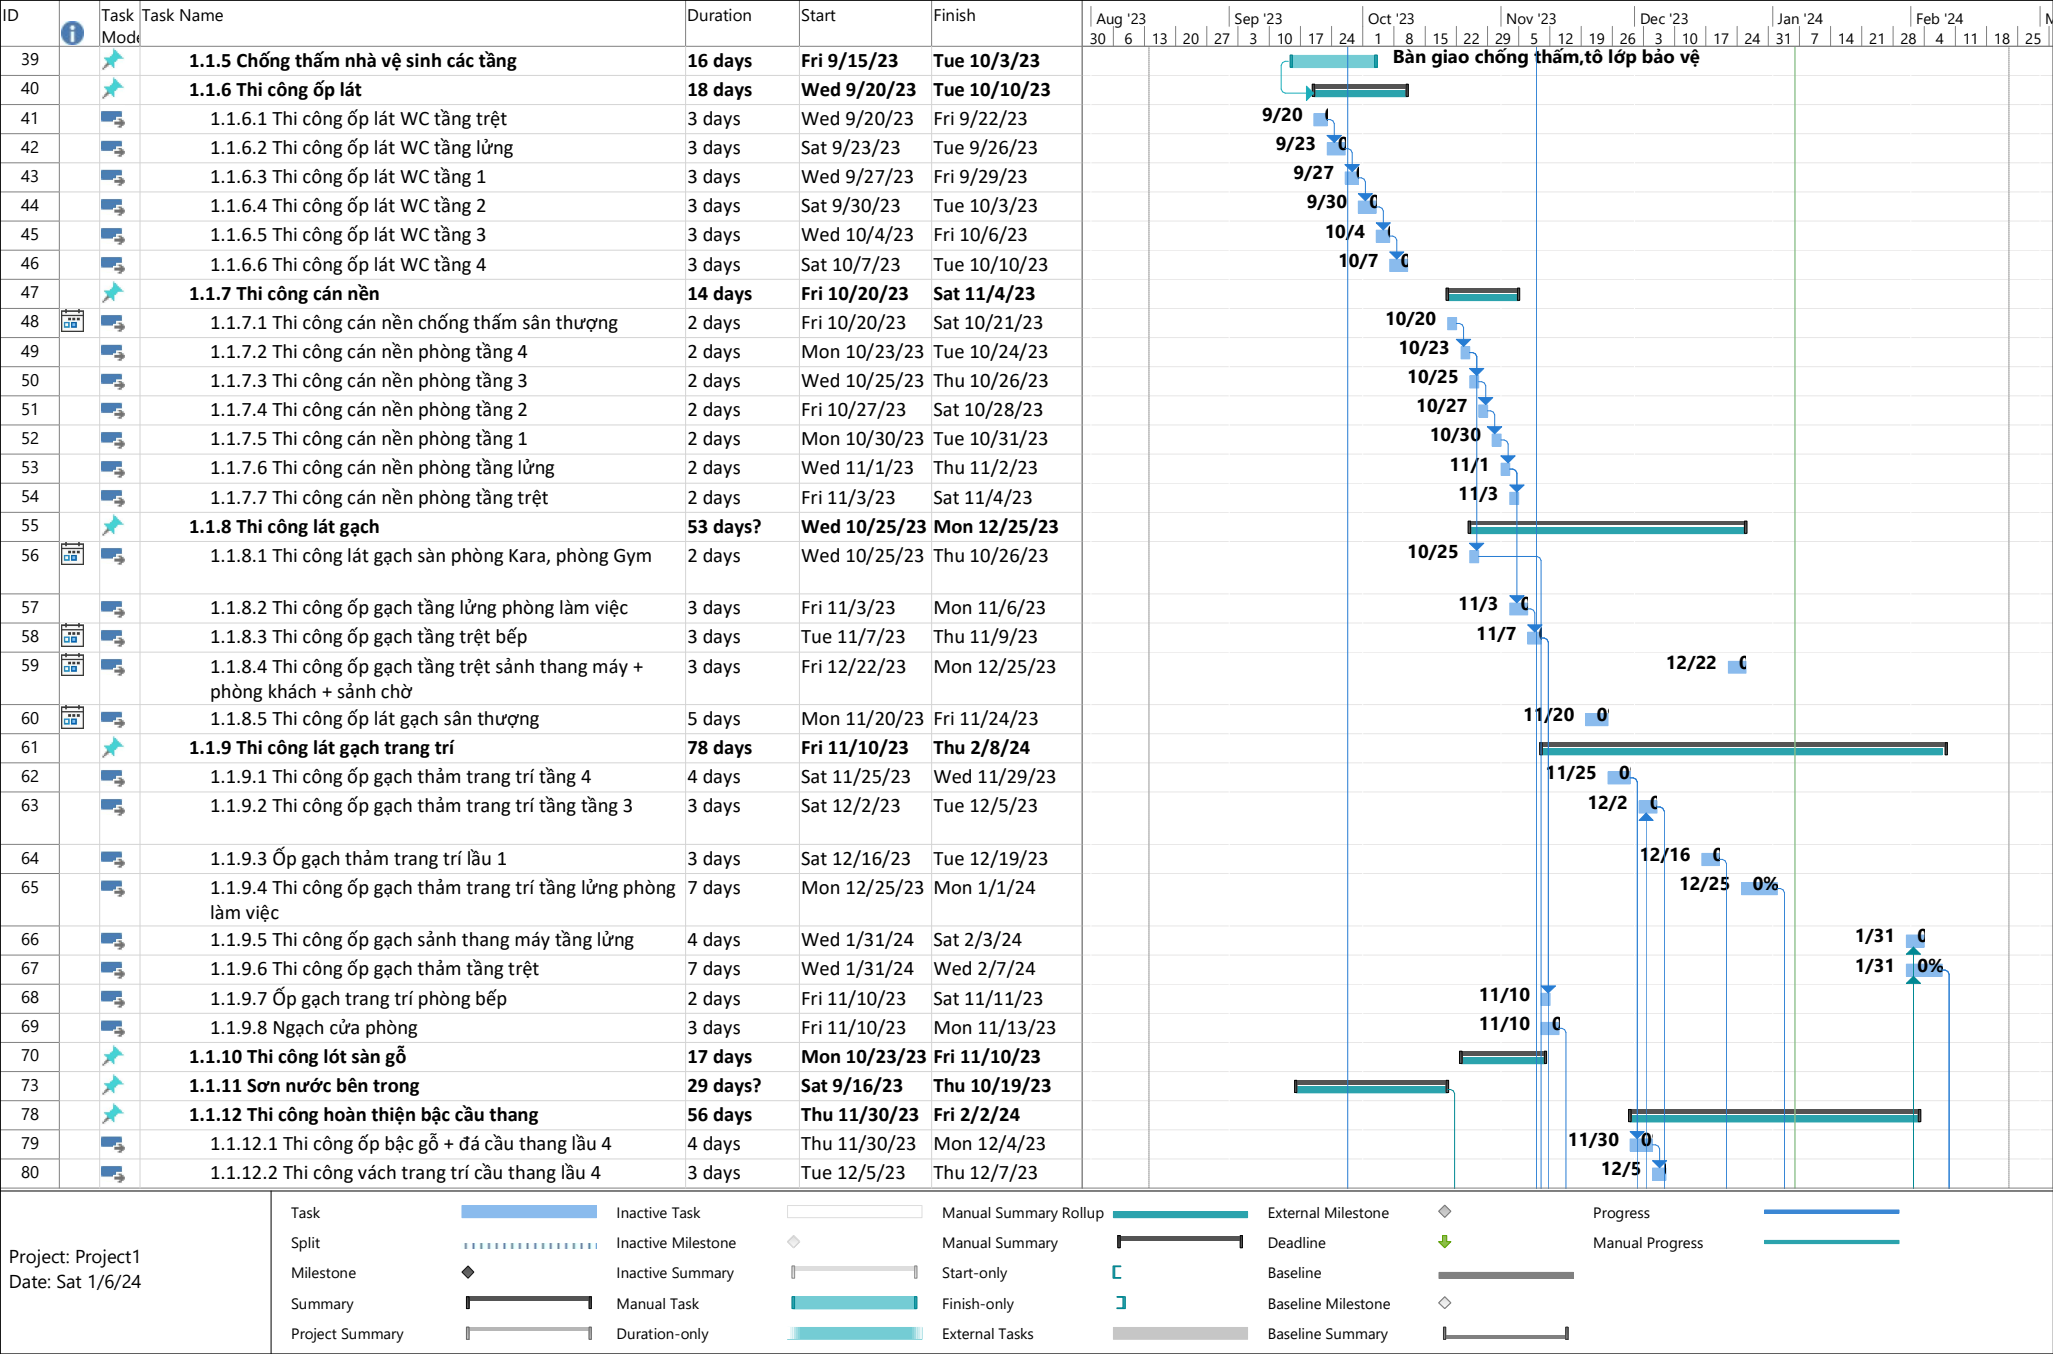

ID	Task Mode	Task Name	Duration	Start	Finish	Aug '23				Sep '23				Oct '23				Nov '23				Dec '23				Jan '24				Feb '24			
						30	6	13	20	27	3	10	17	24	1	8	15	22	29	5	12	19	26	3	10	17	24	31	7	14	21	28	4
133		1.2.1.4.5 Tủ tivi	1 day	Thu 2/8/24	Thu 2/8/24																												
134		1.2.1.5 Sảnh thang máy	81 days?	Thu 11/9/23	Sat 2/10/24																												
135		1.2.1.5.1 Vách đá trang trí sảnh thang máy	1 day?	Thu 2/8/24	Thu 2/8/24																												
136		1.2.1.5.2 Vách gỗ trang trí sảnh thang máy	1 day?	Fri 2/9/24	Fri 2/9/24																												
137		1.2.1.5.3 Gương trang trí bàn console	1 day?	Sat 2/10/24	Sat 2/10/24																												
138		1.2.1.5.4 Bàn console	1 day?	Sat 2/10/24	Sat 2/10/24																												
139		1.2.1.5.5 <New Task>																															
140		1.2.1.5.6 Trần gương trang trí sảnh thang máy	1 day?	Thu 11/9/23	Thu 11/9/23																												
141		1.2.2 Nội thất tầng lửng A Sáng	25 days	Tue 1/2/24	Tue 1/30/24																												
142		1.2.2.1 Hành lang	5 days	Thu 1/25/24	Tue 1/30/24																												
143		1.2.2.1.1 Vách đá trang trí	2 days	Thu 1/25/24	Fri 1/26/24																												
144		1.2.2.1.2 Vách gỗ trang trí sảnh thang máy	2 days	Sat 1/27/24	Mon 1/29/24																												
145		1.2.2.1.3 Amchair	1 day	Tue 1/30/24	Tue 1/30/24																												
146		1.2.2.1.4 Side tap	1 day	Tue 1/30/24	Tue 1/30/24																												
147		1.2.2.1.5 Trần gương trang trí	1 day	Tue 1/30/24	Tue 1/30/24																												
148		1.2.2.2 Phòng làm việc	9 days	Tue 1/2/24	Thu 1/11/24																												
149		1.2.2.2.1 Vách trang trí 2 bên bàn	4 days	Tue 1/2/24	Fri 1/5/24																												
150		1.2.2.2.2 Tủ sách	3 days	Sat 1/6/24	Tue 1/9/24																												
151		1.2.2.2.3 Vách trang trí 2 bên tranh đá	3 days	Tue 1/2/24	Thu 1/4/24																												
152		1.2.2.2.4 Tranh đá	3 days	Fri 1/5/24	Mon 1/8/24																												
153		1.2.2.2.5 Vách kính bên hông	1 day	Tue 1/9/24	Tue 1/9/24																												
154		1.2.2.2.6 Bàn làm việc	2 days	Wed 1/10/24	Thu 1/11/24																												
155		1.2.2.2.7 Ghế bàn làm việc	1 day	Wed 1/10/24	Wed 1/10/24																												
156		1.2.3 Tầng 1 A Tuấn Anh	24 days?	Tue 12/5/23	Mon 1/1/24																												
187		1.2.4 Tầng 2 A Sáng	22 days?	Sat 12/9/23	Wed 1/3/24																												
213		1.2.5 Tầng 3 A Tuấn Anh	18 days	Tue 11/21/23	Mon 12/11/23																												
214		1.2.5.1 Sảnh thang máy	5 days	Wed 12/6/23	Mon 12/11/23																												
215		1.2.5.1.1 Vách trang trí sảnh thang máy	3 days	Wed 12/6/23	Fri 12/8/23																												
216		1.2.5.1.2 Amchair + side tab	1 day	Sat 12/9/23	Sat 12/9/23																												
217		1.2.5.1.3 Trần gương trang trí	2 days	Sat 12/9/23	Mon 12/11/23																												
218		1.2.5.1.4 Tủ console	1 day	Sat 12/9/23	Sat 12/9/23																												
219		1.2.5.2 Phòng ngủ khách	10 days	Tue 11/21/23	Fri 12/1/23																												
220		1.2.5.2.1 Vách trang trí đầu giường	4 days	Tue 11/21/23	Fri 11/24/23																												
221		1.2.5.2.2 Vách tivi	4 days	Tue 11/21/23	Fri 11/24/23																												
222		1.2.5.2.3 Tủ áo	3 days	Sat 11/25/23	Tue 11/28/23																												
223		1.2.5.2.4 Giường ngủ	1 day	Wed 11/29/23	Wed 11/29/23																												
224		1.2.5.2.5 Tap đầu giường	1 day	Thu 11/30/23	Thu 11/30/23																												
225		1.2.5.2.6 Bàn trang điểm + ghế trang điểm	1 day	Thu 11/30/23	Thu 11/30/23																												
226		1.2.5.2.7 Gương soi	1 day	Fri 12/1/23	Fri 12/1/23																												

Project: Project1 Date: Sat 1/6/24	Task		Inactive Task		Manual Summary Rollup		External Milestone		Progress	
	Split		Inactive Milestone		Manual Summary		Deadline		Manual Progress	
	Milestone		Inactive Summary		Start-only		Baseline			
	Summary		Manual Task		Finish-only		Baseline Milestone			
	Project Summary		Duration-only		External Tasks		Baseline Summary			

Page 4

ID		Task Name Mode	Duration	Start	Finish	Aug '23				Sep '23				Oct '23				Nov '23				Dec '23				Jan '24				Feb '24				N			
						30	6	13	20	27	3	10	17	24	1	8	15	22	29	5	12	19	26	3	10	17	24	31	7	14	21	28	4	11	18	25	N
227		1.2.5.2.8 Tủ tivi thấp	1 day	Thu 11/30/23	Thu 11/30/23																																
228		1.2.5.2.9 Amchair + bàn tap	1 day	Thu 11/30/23	Thu 11/30/23																																
229		1.2.5.3 WC phòng ngủ khách	5 days	Sat 11/25/23	Thu 11/30/23																																
232		1.2.5.4 Phòng Spa	12 days	Tue 11/21/23	Mon 12/4/23																																
233		1.2.5.4.1 Ốp đá trang trí tường xung quanh	3 days	Tue 11/21/23	Thu 11/23/23																																
234		1.2.5.4.2 Ốp đá trang trí bồn tắm + bậc thang	3 days	Fri 11/24/23	Mon 11/27/23																																
235		1.2.5.4.3 Vách trang trí bồn tắm gỗ + đá	6 days	Tue 11/28/23	Mon 12/4/23																																
236		1.2.5.4.4 Vách gỗ + đá đen trang trí tủ gội đầu	4 days	Tue 11/21/23	Fri 11/24/23																																
237		1.2.5.4.5 Tủ đứng P. Spa	3 days	Sat 11/25/23	Tue 11/28/23																																
238		1.2.5.4.6 Hệ tủ gội đầu	3 days	Sat 11/25/23	Tue 11/28/23																																
239		1.2.5.4.7 Ốp gỗ phòng Sauna	5 days	Fri 11/24/23	Wed 11/29/23																																
240		1.2.5.4.8 Bộ gương soi đôi khung inox	2 days	Wed 11/29/23	Thu 11/30/23																																
241		1.2.5.4.9 Lắp đặt hệ thống hoàn thiện phòng Sauna	2 days	Thu 11/30/23	Fri 12/1/23																																
242		1.2.6 Tầng 4 A Sáng	20 days	Fri 11/10/23	Sat 12/2/23																																
243		1.2.6.1 Phòng Lounge	20 days	Fri 11/10/23	Sat 12/2/23																																
244		1.2.6.1.1 Hệ vách trang trí	3 days	Thu 11/30/23	Sat 12/2/23																																
245		1.2.6.1.2 Vách trang trí	3 days	Fri 11/10/23	Mon 11/13/23																																
246		1.2.6.1.3 Quầy bar dưới + mặt đá + ghế	5 days	Tue 11/14/23	Sat 11/18/23																																
247		1.2.6.1.4 Kính ốp tường phòng Gym	2 days	Tue 11/14/23	Wed 11/15/23																																
248		1.2.6.1.5 Tủ kệ rượu	2 days	Mon 11/20/23	Tue 11/21/23																																
249		1.2.6.1.6 Ghế Amchair + sidetap	1 day	Wed 11/22/23	Wed 11/22/23																																
250		1.2.6.2 Phòng Karaoke	13 days	Fri 11/10/23	Fri 11/24/23																																
258		1.2.7 Sân Thượng	2 days?	Thu 11/9/23	Fri 11/10/23																																
261			1 day?	Thu 11/9/23	Thu 11/9/23																																

Project: Project1

Date: Sat 1/6/24

Task

Inactive Task

Split

Inactive Milestone

Milestone

Inactive Summary

Summary

Manual Task

Project Summary

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Start-only

Finish-only

Finish-only

External Tasks

External Tasks

External Milestone

External Milestone

Deadline

Deadline

Baseline

Baseline

Baseline Milestone

Baseline Milestone

Baseline Summary

Baseline Summary

Progress

Progress

Manual Progress

Manual Progress
